



اَبُو سَيِّدِي تَكُونُ لَوْ كُنِي مَارَا
UNIVERSITI
TEKNOLOGI
MARA

**FACULTY OF INFORMATION MANAGEMENT
UNIVERSITI TEKNOLOGI MARA (UiTM)
CAWANGAN KELANTAN**

**IM245: BACHELOR OF INFORMATION SCIENCE (HONS) INFORMATION
SYSTEMS MANAGEMENT**

IMS654: INFORMATION SYSTEMS PROJECT MANAGEMENT

Group Project: Project Report

“Providing Financial Information System (fis@usm) Universiti Sains Malaysia”

Prepared by:

AIRUL SHAZWAN BIN NORSHAHIMI	2019336395
ILANI NUR ADRIANI BINTI JASMIN	2019544977
MAZLINA BINTI OTHMAN	2019362005
NOR FATEHA NADILA BINTI MOHD FARIQ	2019717431
NURUL FATIN NASUHA BINTI MOHD FUZI	2019564545

Class:

D1IM2456A

Prepared for:

PN. KHADIJAH ABDUL RAHMAN

Submission date:

1st February 2021

IMS654: INFORMATION SYSTEMS PROJECT MANAGEMENT

Group Project: Project Report

“Providing Financial Information System (fis@usm) Universiti Sains Malaysia

by:

AIRUL SHAZWAN BIN NORSHAHIMI

2019336395

ILANI NUR ADRIANI BINTI JASMIN

2019544977

MAZLINA BINTI OTHMAN

2019362005

NOR FATEHA NADILA BINTI MOHD FARIQ

2019717431

NURUL FATIN NASUHA BINTI MOHD FUZI

2019564545

D1IM2456A

**IM245: BACHELOR OF INFORMATION SCIENCE (HONS) INFORMATION
SYSTEMS MANAGEMENT**

FACULTY OF INFORMATION MANAGEMENT

UNIVRSITI TEKNOLOGI MARA (UiTM)

CAWANGAN KELANTAN

1st February 2021

ACKNOWLEDGEMENT

Alhamdulillah, first of all we would like to thank Allah as finally we were able to finish up our assignment that have been given to us. This task had been done with all afford by our group members even though a little bit problem were happened especially during open distance learning (ODL). Luckily all the problems can be settled down and we were able to adapt properly and wisely.

Besides, that big thank we would address to our lecturer Pn Khadijah Abdul Rahman because without her guidance our assignment cannot be properly completed like this. She always give us supports and guide to us on how to do our assignment in purpose to produce a good outcome.

Finally, thank to our beloved friends that always stick together and also work hard to produce a good assignment with all effort and responsibility. Hope that all the effort will give a lot of benefits to us. Million thank we would like to wish to all our classmates because they also help us in doing this task. They always give us idea and comments due to our work so that we can improve our project in many ways. Thank you.

Once again, we would thanks to everyone especially to those we have mention above.

جَزَاكَ اللهُ خَيْرًا

TABLE OF CONTENT

Content	Page
Acknowledgment.....	i
Table of Content	ii
Preamble.....	1 – 7
1.0 – Initiating Phase	8 – 21
2.0 - Planning Phase	22 – 30
3.0 – Project Scope Management	31 – 39
4.0 – Project Cost Management	40 – 45
5.0 – Project Human Resource Management	46 – 48
6.0 – Project Communication Management	49 – 58
7.0 – Project Risk Management	59 – 63
8.0 – Closing the Project	64 – 67

PREAMBLE

Team Description



Figure 1 Smart Tech logo

Smart Tech company was established in 2015 by Rayyan Adam Bin Rayyan Alif and located in Cyberjaya. Smart Tech company specialized in information system development. The company have main power consist of software, system analyst and programmer. We have a team that have expertise in system development such as planning, analyst, design, implementation and planning. Smart Tech team works for client and give the best way in all desire that the client want. Smart Tech also focusing in performance and use the time given efficiently. Our company also handle more than 30 projects. One of project has been accomplished by our company is development system for e-Financial for Syarikat Muda Osman. And also, second project that we handle is to make system for MyTempahan for company Catering. We also have experience in integrating system with a myriad of third-party software and database, as well as various hardware devices and equipment.

Smart Tech was officially registered with Suruhanjaya Syarikat Malaysia (SSM) and also resisted with the companies Commission of Malaysia [777884-p] in 1 September 2015. Our company also have certificate registration with Ministry of finance mainly verify our qualification to handle system development or software. This certificate as prove that our company are trusted and reliable. Our company has also awarded with the title of the Best system development Awards which the award dedicated to those who build quality code, interoperable across modern browsers and devices for 5 years consequently. This success shows Smart Tech's commitment and dedication to providing its consumers with outstanding support.

Organization Chart f Smart Tech

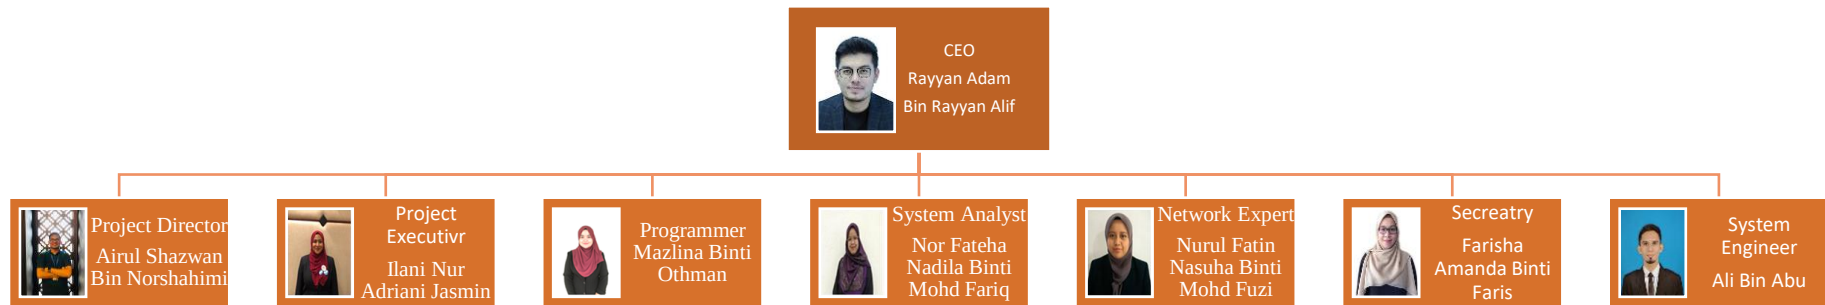


Figure 2 Smart Tech project team organization chart

Vision

To be leading provider of technology system development and digitalization solutions in 2023.

Mission

To provide efficient, reliable and proactive IT support.

Objective

- i. To give the best services of technology system for client
- ii. To produce high quality system that meet or exceed customer requirements.
- iii. To enhance customer satisfaction by complying with the requirement of the Quality Management System (QMS) and continually improving the effectiveness of QMS

Team Member's Profile

AIRUL SHAZWAN BIN NORSHAHIMI

No 18 Lorong Dedalu, Taman Beseri Indah, 02400 Kangar Perlis
phone: +60195178584
email: airulshazwan@gmail.com



Education

UiTM Cawangan Kelantan
Bachelor of Information Science (Hons) Information Systems Management
Current CGPA 3.77

UiTM Cawangan Kedah
Diploma in Information Management
CGPA 3.40

Profile

A passionate person that is interested in improving myself and have experiences in leading teams in international and national projects. Very adaptive to surrounding and a creative problem solver who has consistently completed tasks and projects in time. Extremely motivated to constantly develop my skills and grow professionally.

Achievement & Experience

2020

- Represent UiTM, GLS SDGs by Institut Teknologi Sepuluh Nopember (ITS), Surabaya
- Gold Award, International Information Management Online Showcas (IIMOS) 2020
- Silver Award, CiteFest Championship 2020
- Silver Award, Virtual Innovation Competition 2020 (VIC 2020)

2019

- Represent UiTM, Beijing Foreign Studies University (BFSU) Summer Camp, Beijing.
- Project Manager, PC Tips & Tricks
- Silver Award, Virtual Innovation Competition 2020 (VIC 2020)
- Silver Award, International Innovation & Design in Library &

2018

- Malaysia Delegate for IFLA-WLIC 2018 Kuala Lumpur
- Silver Award, National Student Affairs Invention, Innovation & Design Competition 2018 (NSAIID 2018)
- Committee of International Forum on Function of Languages in Information Search Indonesia, Malaysia & Thailand Perspective in Conjunction with NSAIID 2018)

Skills

Microsoft 365	=====
Leadership	=====
Public Relation	=====
Web Designing	=====
Designing	=====

Language

Malay	=====
English	=====
Mandarin	=====


Reference

Mohammad Akmal Faiz Osman
Akmalfaz@uitm.edu.my
+60137788494

Figure 3 Project manager's profile

ILANI ADRIANI

UNIVERSITY STUDENT

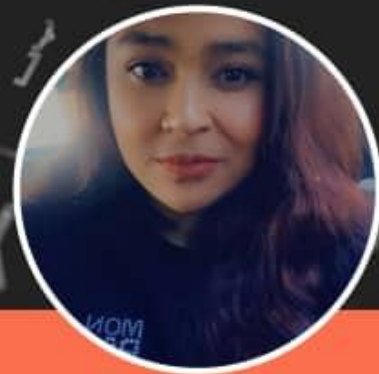

Work History

FNB ASSISTANT

LONE PINE HOTEL | 2015- 2016

- Perform tasks related to ensuring compliance with safe food prep and handling, storage and sanitation.
- Assists in working with vendors, ordering food products and beverages.
- Assist staff scheduling, overseeing maintenance requests, and ensuring patrons have an enjoyable experience with the establishment.

SALES EXECUTIVE

BENJAMIN HOME | 2020

- Promote products and services to customers and negotiate contracts with the aim of maximizing profits.
- Actively seeking out new sales opportunities through cold calling, networking and social media.
- Prepare and deliver appropriate presentations on products and services

Education History

UNIVERSITI TEKNOLOGI MARA, KELANTAN

Bachelor of Information Science (HONS) Information Systems | 2019 - present

- BEST SPEAKER: ASEAN University Student Leadership Conference
- BEST DEBATER: Piala Debat Sultan Zainal Abidin
- InDeLib Innovation, won silver award
- VIC 2020 competition, won silver award
- Malaysia Youth Leaders Assembly (MYLA) participants

UNIVERSITI TEKNOLOGI MARA, KEDAH

Diploma of Information Management | Class of 2016

- Graduated with a 3.63 CGPA
- Three times Dean's Award winner
- Secretary of Student Representative Council 17/18
- INFORMA Club highest council, secretary
- Captain of faculty's parade team, won 1st place
- IID Competition, bronze award

Personal Profile

I am an active university student with a great passion for all aspects including leadership, and I intend on working towards a career in diverse field. I look forward to challenges and new knowledge.

Contact Details

Tanjung tokong, Georgetown 10470 Penang.



adrianijasmin@gmail.com

016-5560451

Notable Skills

- Time management and organization
- Oral and written communication
- Creative problem-solving, initiative and enterprise
- Critical and analytical thinking
- Ability to apply discipline, knowledge and concepts

Reference

Dr. Nor Erlissa Abd Aziz
Senior Lecturer of Faculty Information Management
016-5007599

Dr. Abd Latif Abdul Rahman
Deputy Rector Student Affairs Division
019-5584030

Figure 4 Deputy Project Manager's profile



Figure 5 Programmer's profile



Figure 6 Network Expert's profile

NURUL FATIN NASUHA



A multi-tasker, hardworking and creative young talent with commendable technical skills and leadership

PERSONAL INFORMATION

Name : Nurul Fatin Nasuha Bt Mohd Fuzi
Age : 24 Years Old
Nationality: Malaysian
Health : Excellence

CONTACT INFORMATION

Phone : +60134003563
Email : nurulfatinnasuhafuzi@gmail.com
Address : 766-D, Kampung Bunut Payong,
15150, Kota Bharu, Kelantan

ACADEMIC BACKGROUND

2019-current: **Universiti Teknologi Mara (UiTM)
Kelantan**
*Bachelor of Information Science (Hons)
Information System Management.*

2015-2019 : **Universiti Teknologi Mara (UiTM)
Kelantan**
Diploma in Information Management

2014 : **Sijil Pelajaran Malaysia (SPM)**

LANGUAGE SKILLS

- Malay
- English
- Arabic
- Chinese

SOFTWARE SKILLS

- HTML
- PHP
- CSS
- Microsoft Office
- Adobe Premier Pro
- Adobe Photoshop
- Adobe InDesign

ACTIVITIES AND ACHIEVEMENTS

1. Gold Award of International Information Management Showcase (IIMOS) 2020
2. Silver Award of Virtual Innovation Competition 2020
3. Society of Information System Management

REFERENCES

MADAM IZZATIL HUSNA BINTI ARSHAD
Senior Lecturer,
Faculty of Information Management
Universiti Teknologi MARA
(UiTM), Kelantan Branch,
019-6976693
husna672@uitm.edu.my

SIR MOKHD AKMAL FAIZ BIN OSMAN
Lecturer/Industrial Training Coordinator
Information System Management,
Universiti Teknologi MARA (UiTM), Kelantan
Branch,
013-7788494
akmalfaiz@uitm.edu.my

Figure 7 System Analyst's profile

1.0 – INITIATING PHASE

1.1 Introduction

According to APM Body of Knowledge 7th edition, project management is determined as an application of processes, methods, skills, knowledge, and experience in order to achieve specific project objectives based on project acceptance criteria within the agreed scales. Project management includes final deliverables that are constrained to a finite timescale and budget. Dr. Martin Barnes further clarify that a key factor ought to distinguish a project management from an ordinary management is that it has the final deliverable and a finite timespan, unlike management which is considered as ongoing process. This is due to the fact that, a project professional needs a wide range of skills, often technical skills, and certainly people management skills and good business awareness.

According to Kate Eby (2018), there are several phases in project management to which it also includes project initiation as the initial phase. For the earlier stage, the primary key step that a project manager ought to take when initiating a new project is to create a trade case. A trade case document is the formal start of the project when the project sponsor or the project initiator gives a depiction of the business problem and opportunity. The project is to be started to address the issue or provide alternative solutions. The trade case project will incorporate the commerce issue and potential costs related with the project implementation.

Next, the second key step that a project manager ought to take when starting a new venture is to make a visibility study. A visibility study is a research conducted to decide whether the project can be accomplished and to distinguish the probability of the alternative solutions. The feasibility study explores whether the benefits expressed within the business case can be delivered. It also portrays relationship of trade or so-called business costs with the project solutions.

Moreover, the third key step that a project manager ought to take when starting a new project is to create a project charter. Once the business issue and opportunity as well as possible solutions have been distinguished, the following step is to create a project charter which is the most essential document of the initiation phase. The project charter basically portrays the particular project sets out to unravel the business issue and what the boundaries of the project will be. It indicates the project vision, objectives and goals, scope and boundaries, deliverables and expectations, project organization and an implementation plan.

Other than that, the fourth key step that a project manager ought to take when starting a new project is to assign the project management group. The project constitution is created to ensure that the team would be able to proceed with recognizing human resources required in order to deliver the project and achieving its objectives. A project manager will have to delegate the management group member who is able to uphold the primary obligation for the planning and execution of the project. The project committee ought to be established, and the project manager ought to be appointed to ease the process. At that point the project manager will work on enlisting the project team and making project assignments.

In the last stage, the fifth key step that a project manager ought to take when starting a new project is perform a project review. The final step that a project manager must take through the project initiating stage is on analyzing the project. A review stage ought to be conducted to determine that the project is effectively started which this implies all the initiation activities are completed. Once the project is reviewed on and the project planning stage is begun (Eby, 2018).

1.2 Project Integration Management

According to Schwalbe (2015), Project Integration Management is known to be the integration of all the method and activities included in identifying, characterizing, combining, binding together and planning the different forms in the project administration. Project Integration Management is an essential portion for the successful completion of a project because it makes a difference in coordination all the processes of the project and maximizes the execution to attain the fruitful completion of the project throughout the whole life cycle of the project. The project manager is dependable for a compelling project integration strategy as the victory of any project is exceedingly subordinate to it and makes a difference for stakeholders' fulfilments.

There are six process of Project Integration Management that set up by Smart Tech Sdn. Bhd. which functions for Project Charter development, creating the, Directing and Managing Project Execution, Monitoring and Controlling Project Work, Performing Coordinates Change Control, and Closing the Project or Stage (Schwalbe,2015).

1.2.1 Pre-Initiating Phase

The tender category being identified is software services to which Smart Tech has decided to propose a tender in order to provide financial Information System for Universiti Sains Malaysia. The business case displays the description of the project.

1.2.1.1 Business case

Table 1 Project Business case

PROJECT BUSINESS CASE			
Project Name	Implementation of Financial Information System @ USM		
Project sponsor	Universiti Sains Malaysia		
Project Manager	Airul Shazwan B Norshahimi		
Date of Project Approval	27 December 2020	Last Revision Date	27 December 2020
Contribution to Business Strategy	The company strategy is to ensure the provision of Financial Information System for Universiti Sains Malaysia with excellent performance.		
Options considered	1. Provide timely, accurate and consistent financial data for management and decision making 2. Client observation on team members contribution 3. Adequate budget for hardware, software, and maintenance process		
Benefits	1. Create network- the project ought to be executed with the collaboration between the company and USM 2. Security and confidentiality- the need of FIS is to ensure all data is encrypted upon and assure its confidentiality 3. Significant productivity- the project ought to improve its productivity by implementing significant performance of financial information system		

Timescale	The time scale requires full 4 months to implement the installation of FIS in Universiti Sains Malaysia and to test the performance of the system and continue to provide maintenance back up on hardware and software for 3 years.
Costs	RM298,094.40
Expected ROI	121 % / RM319,050.47
Constraints	The risks within the project is to meet the client's requirements. The project ought to implement a financial information system in order to maintain the business activity. However, there shall be the provision of maintenance to improve and update the FIS at it will need better version at a certain period of time. Hence, it will be difficult to fulfil the client's expectation that changes several times.

1.2.1.2 Business case Financial Analysis

Net Present Value (NPV)

Table 2 Net Present Value (NPV)

Discount rate	9%					
	Month 0	Month 1	Month 2	Month 3	Month 4	Total
Costs	RM119,237.76	RM44,714.16	RM44,714.16	RM44,714.16	RM44,714.16	RM298,094.40
Discount factors	1	0.92	0.84	0.77	0.71	
Discount cost	RM119,237.76	RM41,022.17	RM37,635.01	RM34,527.54	RM31,676.64	RM264,099.11
Benefits	0	RM180,000.00	RM180,000.00	RM180,000.00	RM180,000.00	RM720,000.00
Discount factor	1	0.92	0.84	0.77	0.71	
Discount benefits	0	RM165,137.61	RM151,502.40	RM138,993.03	RM127,516.54	RM583,149.58
Discounted benefits - cost	-RM119,237.76	RM124,115.45	RM113,867.38	RM104,465.49	RM95,839.90	RM319,050.46
Cummulative benefits - cost	-RM119,237.76	RM4,877.69	RM118,745.07	RM223,210.57	RM319,050.46	
		↑				↑
		Payback in Month 1				NPV
Return of Investment (ROI)	→	121%				

NPV is total discounted benefits minus total discounted costs which is RM319,050.46.

Discount Factor

The formula for discount factor is $1/(1+r)^t$ where r is the discount rate and t is the year.

$$\text{Year 0: discount factor} = 1/(1+0.09)^0 = 1$$

$$\text{Year 1: discount factor} = 1/(1+0.09)^1 = 0.92$$

$$\text{Year 2: discount factor} = 1/(1+0.09)^2 = 0.84$$

$$\text{Year 3: discount factor} = 1/(1+0.09)^3 = 0.77$$

$$\text{Year 4: discount factor} = 1/(1+0.09)^4 = 0.71$$

Return on Investment (ROI)

Return on Investment = (Total Discounted Benefits – Total Discounted Cost) / Total Discounted Cost

$$\text{ROI} = (\text{RM}583,149.58 - \text{RM}264,099.11) / \text{RM}264,099.11$$

$$= \text{RM}319,050.47 / \text{RM}264,099.11$$

$$= 1.208 \times 100\%$$

$$= 120.8\%$$

Return on Investment (ROI) = 121%

Payback Chart

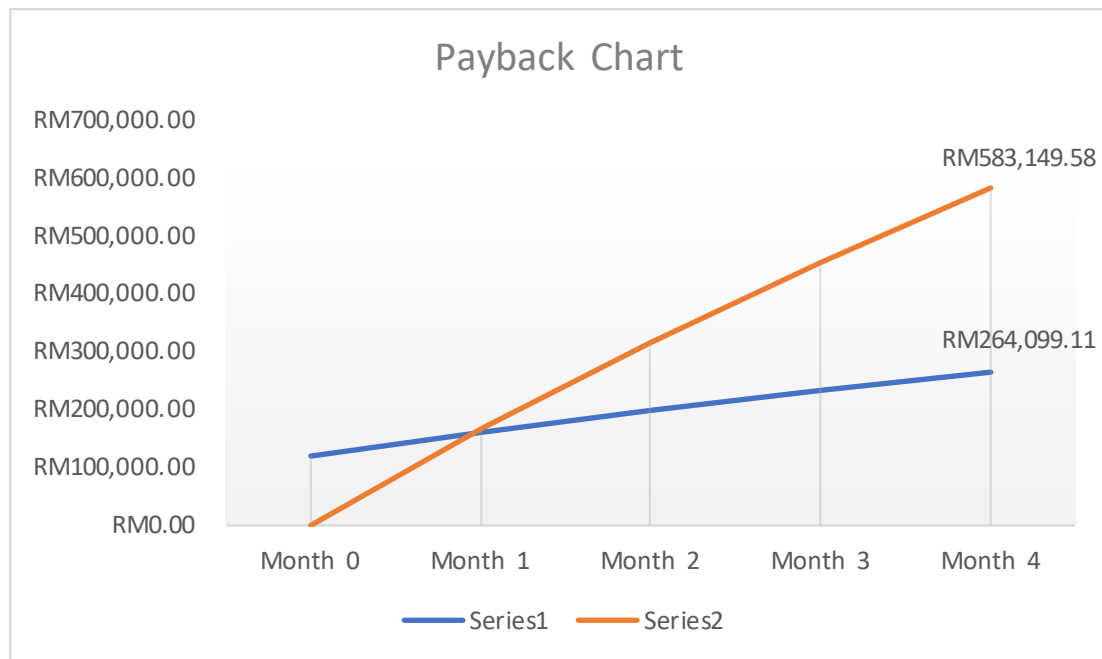


Figure 8 Payback Chart

Table 3 Payback chart details

Payback Chart		
Year	Cummulative cost	Cummulative benefits
Month 0	RM119,237.76	RM0.00
Month 1	RM160,259.93	RM165,137.61
Month 2	RM197,894.94	RM316,640.01
Month 3	RM232,422.47	RM455,633.04
Month 4	RM264,099.11	RM583,149.58

The figure 8 and table 3 shows the precise payback period which is on year 1. Based on the figure 8, the blue line represents cumulative cost and the red line represents cumulative benefits. The table 3 shows on the payback chart details from month 0 to month 4

1.2.1.3 Stakeholder Register

Table 4 Stakeholder register

NAME	POSITION	INTERNAL/ EXTERNAL	PROJECT ROLE	CONTACT INFORMATION
Prof Dr. Faisal Rafiq	Vice-Chancellor of USM	External	Sponsor	FaisalRadiq@edu.my
Rayyan Adam Bin Rayyan Alif	CEO of Smart Tech Sdn. Bhd.	Internal	Sponsor	rayyanadam@Smartech.my
Airul Shazwan B Norshahmi	Project Management Office Director	Internal	Project Manager	airulshazwan@smartech.my
Ilani Nur Adriani Bt Jasmin	Team member	Internal	Deputy Project Manager	ilaniadraini@smartech.my
Mazlina Bt Othman	Team member	Internal	Programmer	mazlinaothman@smartech.my
Nor Fateha Nadila Bt Mohd Fariq	Team member	Internal	System analyst	fatehafariq@smartech.my
Nurul Fatin Nasuha Bt Mohd Fuzi	Team member	Internal	Network expert	fatinasuha@smartech.my
Khoo Boon Lim	CEO of Rapid Cloud Malaysia	External	Sponsor	kbl@rapidcloud.my
Joshua A/L Muthu	Software Engineer Officer	External	Sponsor	joshua@rapidcloud.my

1.2.1.4 Stakeholder Management Strategy

Table 5 Stakeholder management strategy

Name	Level of Interest	Level of Influence	Potential Management Strategies
Prof Dr. Faisal Rafiq	High	High	Prof Dr. Faisal Fariq is the client of the project. It is essential to keep him update on the progress and remind him that he is a part of the team.
Rayyan Adam B Rayyan Alif	High	High	Mr. Andrew is the CEO of the company who is very professional. Keep him informed of the key constraints and never let anything surpass him.
Airul Shazwan B Norshahimi	High	High	As the project manager, Airul Shazwan is known to be team-driven, creative minded and well-organized that makes him easy to work.
Ilani Nur Adriani Bt Jasmin	High	Medium	Ilani is the deputy who determine to ensure contingency plan is prepared and ought to be executed with excellence.
Mazlina Bt Othman	High	Low	As the project programmer, Mazlina is multitasking. She able to work on the framework and ensure the progress is done smoothly.
Nor Fateha Nadial Bt Mohd Fariq	High	Low	As system analyst, Fateha is known to be very meticulous with her work. She ought to finish her tasks in orderly manner.
Nurul Fatin Nasuha Bt Mohd Fuzi	High	Low	As the team's network expert, Fatin is an important person to which she is responsible of connection from all aspects.
Khoo Boon Lim	High	Medium	The CEO of Rapid Cloud is the sponsor of several well-established projects. Therefore, it is importance to provide him with the status on the project development.
Joshua A/L Muthu	Medium	Low	Joshua works with Rapid Cloud. Therefore, his contribution is significant to the project which is why it is vital to ensure all progress is within the time frame.

1.2.2 Initiating Phase

1.2.2.1 Kick-off Meeting

MINUTES OF MEETING FOR PROJECT DEVELOPMENT

Minutes of Kick-off Meeting of the Committee Members was held on Monday, 27 December 2021 at 10.00 a.m. in the Google Meet

PRESENT:

- Airul Shazwan Bin Norshahimi (Project Manager)
- Ilani Nur Adriani Binti Jasmin (Deputy Project Manager)
- Mazlina Binti Othman (Programmer)
- Nor Fateha Nadila Binti Mohd Fariq (System Analyst)
- Nurul Fatin Nasuha Binti Mohd Fuzi (Network Expertise)

1. Project Manager Welcome Address

The Project Manager Called the meeting to order at 10.00 am and welcomed all the members.

2. Apologies for Absence

No apologies for absence were received at that meeting.

3. Special Business

This meeting will be discussing the goal and future of the project and also the budget allocated for the project.

4. Date, Time and Venue of the Next Meeting

It was also decided that the next meeting will be held on 1st January 2021, in the Google Meet. The time would be confirmed by the secretary later.

5. Close

The project manager thanked all the team members for their participation during the meeting session and adjourned the meeting at 12 p.m.

.....

Signed by

Mr. Airul Shazwan Bin Norshahimi

Project Manager

.....

Date

.....

Recorded by

Ms. Farisha Amanda Binti Faris

Secretary

.....

Date

Figure 9 Kick-off minutes of meeting

1.2.2.2 Project charter

The project charter selected by our company is the project with Universiti Sains Malaysia (USM) which request the execution of financial system in the campus.

Table 6 Project charter

Project Title: Implementation of FIS in Universiti Sains Malaysia	
Project Start Date: 30 December 2020	Project Finish Date: 30 April 2021
Key Schedule Milestone: • Complete the implementation of financial framework of Universiti Sains Malaysia by 15 April 2021 • Complete testing on the execution of Financial Information System by 25 March 2021 • Contract for maintenance and warranty for 3 years onwards	
Budget Information: The organization has allocated RM298,094.40 for the project development. Most budget for this project development incurred for hardware, labor cost, and maintenance cost.	
Project Manager: Airul Shazwan Bin Norshahimi	
Project Objectives: The objective of this project development is to ensure excellent performance of FIS implemented for Universiti Sains Malaysia within the time frame given and to ensure completion of testing based on the schedule milestone. The period of project development took up 4 months and ought to have maintenance contract up to 3 years. It is an essential project for the company. This is the first charter of the project and ought to be developed with excellence.	
Main Project Success Criteria: The financial Information System will be able to meet all of the agreed upon specifications, be well examined, and executed within the time frame. The CEO will formally approve the project with advice from other stakeholders. The project should pay for itself within two years upon completion.	

1.3 Appendix (Minutes of meeting)

MINUTES OF MEETING FOR PROJECT DEVELOPMENT

Minutes of Kick-off Meeting of the Committee Members was held on Monday, 27 December 2021 at 10.00 a.m. in the Google Meet

PRESENT:

- Airul Shazwan Bin Norshahimi (Project Manager)
- Ilani Nur Adriani Binti Jasmin (Deputy Project Manager)
- Mazlina Binti Othman (Programmer)
- Nor Fateha Nadila Binti Mohd Fariq (System Analyst)
- Nurul Fatin Nasuha Binti Mohd Fuzi (Network Expertise)

1. Project Manager Welcome Address

The Project Manager Called the meeting to order at 10.00 am and welcomed all the members.

2. Apologies for Absence

No apologies for absence were received at that meeting.

3. Special Business

This meeting will be discussing the goal and future of the project and also the budget allocated for the project.

4. Date, Time and Venue of the Next Meeting

It was also decided that the next meeting will be held on 1st January 2021, in the Google Meet. The time would be confirmed by the secretary later.

5. Close

The project manager thanked all the team members for their participation during the meeting session and adjourned the meeting at 12 p.m.

.....	
Signed by	Date
Mr. Airul Shazwan Bin Norshahimi	
Project Manager	
.....	
Recorded by	Date
Ms. Farisha Amanda Binti Faris	
Secretary	

Figure 10 Minutes of meeting for project development

1.4 References

- Eby, K. (2018). *Demystifying the 5 Phases of Project Management*. Smartsheet.
<https://www.smartsheet.com/blog/demystifying-5-phases-project-management>.
- What is project management?* <https://www.apm.org.uk/resources/what-is-project-management/>.

2.0 – PLANNING PHASE

2.1 Introduction of Planning phase

Lucidchart Content Team (2021) indicates project planning is an important phase in the project management life cycle which is to ensure the project becomes successful. In the project management life cycle, project planning involves help and guidance from each member. Project planning phases are usually made to support the organization in managing time, cost, risk, related issues and defining what needs to be done in the project management life cycle.

Project planning phase in the organization can help the staff and external suppliers in delivering the project. Most challenging part for a project manager in the project management life cycle is when he needs to make a quality plan for his staff, resources, equipment and supplier to accomplish this project (Watt, 2014).

In the project planning phase, the company should have an effective plan for communication and procurement activities. Furthermore, the project planning process includes creating workflow diagrams, estimating project budget, creating financial plans, gathering all the resources, solution for the potential risk and meeting for each phase in the project management life cycle (Watt, 2014).

2.2 Project Integration Management + Project Scope Management

2.2.1 Introduction

Based on Project Management Professionals article (2021) Project Scope Management refers to creating all the work involved in the deliverable of the project such as meeting minutes and planning documents. In the Project Scope Management Process, this process will cover team contract, scope of this project, statement of work (SOW) and change request form. Team contract refers to who is involved in project development and how team members coordinate the project. Purpose of team contracts are to help and support the team members in creating the project. All the duties and responsibilities of team members should be included in team contracts.

Next, William (2021) studied scope statement. Scope statement is a written documented confirmation of the results for the project and typically written by a project manager which is very vital in the project. In addition, a statement of work or known as SOW should be covered in this process. Statement of work (SOW) is a formal documentation that includes all the roles

and responsibility of the employees, cost, deliverables and all the entire work that is involved in this project.

Change request form is a form to change the system, hardware and some equipment in the project. For example, Project Managers are using change request form to request changes of the scope, goals, mission, vision and objectives of the project (Portny, 2021)

2.2.2 Team contract

Project Name : Implementation of Financial Information System for Universiti Sains Malaysia (USM)

Project Team Member's Name:

1. Airul Shazwan Bin Norshahimi
2. Ilani Nur Adriani Binti Jasmin
3. Mazlina Binti Othman
4. Nor Fateha Nadila Binti Mohd Fariq
5. Nurul Fatin Nasuha Binti Mohd Fuzi\

Commitments

As a project team, we will

- i. Be honest and realistic in planning and reporting the project.
- ii. Only agree to do work that has qualification and ability to do.
- iii. Ensure the team members are engaged in effective communication and keep updated upon the development.
- iv. Operate the whole project management process in a proactive manner and detect the potential problems in the project.
- v. Focus on what is the best for the whole project.

Participant

As a project team, we will:

- i. Be honest and open-minded during meetings
- ii. Encourage feedback on the topic discussed.
- iii. Give everyone the opportunity to participate equally during the meetings.
- iv. Be open and listen to new approaches as well as provide innovative suggestions.
- v. Keep the issues from arising during meetings unless the teams highlighted it.

Communication

As a project team, we will:

- i. Remove distractions during conversations.
- ii. Be open to constructive criticism.
- iii. Encourage team members to remain honest when discussing ideas.
- iv. Make it a discussion to keep on track.
- v. Ask questions when ideas are not clear

Meeting Guideline

As project team we will:

- i. Be prepared to effectively and efficiently contribute in order to achieve the meeting goals.
- ii. Agenda meeting must be discussed at the end of each meeting.
- iii. Be patient when listening to others speak and do not interrupt them.
- iv. Unresolved issues will be added to the issues list.
- v. Post minutes meeting and important documents through email.

2.2.3 Scope statement

The purpose of the Project Scope Management is to provide understanding and criteria scope of the project among the stakeholders. Therefore, below is the project scope statement for Implementation of Financial Information System for Universiti Sains Malaysia:

Table 7 Scope statement

CRITERIA	DESCRIPTION
Project Scope Description	Implementation of Financial Information System for Universiti Sains Malaysia is to provide good services for their staff, students and users.
Project Deliverables	To facilitate and track the expansion of financial status and financial crisis in the Universiti Sains Malaysia by provide financial information system to the university.
Project Assumptions	To be able to implement the financial information system project for long term used and user-friendly through staff, student and public users.
Project Constraints	Lack of maintenance cost, hardware and software.
Project Boundaries	Insufficient of resources and lack of professional staff in dealing with the marketing.
User Acceptance Criteria	Smart Tech should create and provide the effectiveness of financial information system between their staff, students and publics in their university.

2.2.4 Statement of work

According to project management guide (2021), Statement of Work or SOW is a formal documentation that includes all the responsibility of the employees, cost, deliverables and all the entire scope of work involved in this project. A Statement of work (SOW) should explain to all their stakeholders when disputes happen. Furthermore, a statement of work (SOW) must provide due dates of the project, purpose of the project, the deliverables and what the expected outcomes in the project.

i. Scope of Work

There are five staff that are involved in the implementation of the financial system for Universiti Sains Malaysia (USM) which each their position as well as Project Manager, Deputy

Project Manager, Programmer, System Analyst and Network Expert. First of foremost, A project manager is responsible to ensure all the processes in the project management life cycle such as initiating, planning, designing, executing, monitoring, controlling and closure of the project could be operated. A project manager has skill to resolve all the problems in the project. While, the Deputy Project Manager is responsible to be able to work with the project manager and ensure the project runs smoothly. A Deputy Project Manager is required to assist the project manager in order to complete the project. Another position, a programmer, who is responsible to maintain and troubleshoot the hardware and software of the system. Programmer are responsible for designing, testing and detecting the problems in the system. Next position in implementation of the financial system for Universiti Sains Malaysia is system analyst. System analyst is a person who is responsible for developing the software and hardware solutions in the system. A System Analyst also will lead the training session for the clients and project team members. Last position in this project is our network expert. She is responsible to manage the networks and system could work effectively (Monappa, 2021).

ii. Location of Work

Location for our planning and implementing phase, it will be conducted at SMART Tech Office while for the project marketing, it will be held at client's office.

iii. Period of Performance

The development of this project ought to be completed within 120 days excluding weekends. Our development period initiated on 30 December 2020 until 30 April 2021.

iv. Acceptance Criteria

Our company, **Smart Tech** standard is to provide solutions for the financial information system in Universiti Sains Malaysia. Before the system can be implemented and launched for the clients at USM, the team members will test the system first before releasing it to our customers. Therefore, if the stakeholders of this system are not satisfied with this system and did not meet with their requirements. Our staff will improve and check which part of the system should be upgraded or modified.

v. Special Requirements

For the special requirements, Nor Fateha Nadila as the system analyst will conduct research on the financial information system requirement and clarify to all the members of

these projects. After that, our programmer will maintain, debug and troubleshoot the system while for our system analyst, she will design the system to make it attractive. Our team members have qualifications, skills, background in working experience and are able to organize this project outstanding than what expected of our clients.

2.2.5 Change request form



SERVICE CHANGE REQUEST FORM

CHANGE REQUEST FORM		
PROJECT NAME'S :	DATE:	
CHANGE REQUESTOR NAME'S:	CHANGE NO:	
CHANGE CATEGORY (PLEASE TICK ☒ APPROPRIATE BOX BELOW): ☐ Enhancement ☐ Defect ☐ Other		
DESCRIBE THE CHANGE BEING REQUESTED		
DESCRIBE THE REASON FOR THE CHANGE		
DESCRIBE RISKS TO BE CONSIDERED FOR THIS CHANGE		
ESTIMATE COST NEEDED TO IMPLEMENT THIS CHANGE		
CHANGE STAFF APPROVAL:		
NAME	SIGNATURE	DATE

Figure 11 Change request form

2.3 Appendix (Minutes of meeting)

MINUTES OF MEETING FOR PROJECT DEVELOPMENT

Minutes of second Committee Meeting of the Committee Members was held on Friday, 1st January 2021 at 10.00 a.m. in the Google Meet

PRESENT:

- Airul Shazwan Bin Norshahimi (Project Manager)
- Ilani Nur Adriani Binti Jasmin (Deputy Project Manager)
- Mazlina Binti Othman (Programmer)
- Nor Fateha Nadila Binti Mohd Fariq (System Analyst)
- Nurul Fatin Nasuha Binti Mohd Fuzi (Network Expertise)

1. Project Manager Welcome Address

The Project Manager Called the meeting to order at 10.00 am and welcomed all the members.

2. Apologies for Absence

No apologies for absence were received at that meeting.

3. Special Business

This meeting will be discussing the planning phase.

- Build team contract
- Identify project scope statement
 - Each system has their own scope work
 - Scope of work identify through system requirement
- · Change request form.

4. Date, Time and Venue of the Next Meeting

It was also decided that the next meeting will be held on 1st February 2021, in the Google Meet. The time would be confirmed by the secretary later.

5. Close

The project manager thanked all the team members for their participation during the meeting session and adjourned the meeting at 12 p.m.

.....

Signed by

Mr. Airul Shazwan Bin Norshahimi

Project Manager

.....

Date

.....

Recorded by

Ms. Farisha Amanda Binti Faris

Secretary

.....

Date

Figure 12 Minutes of meeting for project development

2.4 References

- Lucidchart Content Team (2021). The 4 Phases of the Project Management Life Cycle. Retrieved from <https://www.lucidchart.com/blog/the-4-phases-of-the-project-management-life-cycle>
- Portny, E. Stanley. (2021). What to Include in a Project Scope Statement. Retrieved from <https://www.dummies.com/careers/project-management/what-to-include-in-a-project-scope-statement>
- Sample Team Contract. (2021). Retrieved from http://www.pmtraining.com.tw/member_pmp/Team%20Contract%202.0.pdf
- Watt, A. (2014). *8. Overview of Project Planning*. Project Management. <https://opentextbc.ca/projectmanagement/chapter/chapter-8-overview-of-project-planning-project-management/>.
- What is Project Scope Management?. (2021). Retrieved from <https://www.invensislearning.com/articles/pmp/what-is-project-scope-management>
- William, M. (2021). How to Make a Scope Management Plan. Retrieved from <https://www.projectmanager.com/blog/scope-management-plan>

3.0 – PROJECT SCOPE MANAGEMENT

3.1 Introduction

Project Management Professionals, PMP (2021) Project Scope Management refers to creating the products of the project and all the work that involves in the deliverable of the project such as meeting minutes and planning the documents. Scope management enables a project manager to allocate the resources of work.

3.2 Work breakdown structure

According to A Guide to the Project Management Body of Knowledge (PMBOK Guide) defines that work breakdown structure is a deliverable-oriented hierarchical decomposition of the work that must clearly demonstrate the relationship between deliverables of the project. Work breakdown structure (WBS) also ought to execute deliverable project and project manager will determine the outcome of the project development.

Table 8 Work breakdown structure (WBS)

WORK BREAKDOWN STRUCTURE (WBS)		
1.0	INITIATION	
	1.1	Create trade case
	1.2	Feasibility study
	1.3	Develop a Project Charter
	1.4	Assign the Project Management Group
	1.5	Perform a Project Review
2.0	PLANNING	
	2.1	Project meeting
	2.2	User requirement
	2.3	Set up project requirement
	2.4	Determine project benefits
	2.5	Draft project planning and cost
	2.6	Develop scope statement
	2.7	Create WBS
	2.8	Meeting

3.0	EXECUTING	
	3.1	Project progress
	3.2	Installation
	3.3	Training
	3.4	Develop training documentation
4.0	MAINTENANCE & CONTROLLING	
	4.1	Corrective manner
	4.2	Adaptive manner

1.0 Initiation

In the initiation phase, a project manager will initiate this project by creating a trade case document. A trade case document is a formal start to provide an overview of business problems, address the issues and the alternative solution for this project. A trade case document will incorporate the potential cost that is related to the project implementation. After that, a project manager will make a feasibility study for the project. Feasibility study is used to investigate the benefits of the business case, can be delivered and understand all the aspects of a project, such as planning of a project. During doing feasibility study, a project manager should provide a solution to distinguish the potential problems and risk. Next, create a project charter. The project charter indicates the objectives, goals, vision, scope and boundaries, deliverables and expectations, project organization and an implementation plan which is to ensure the projects will meet the user requirements. Besides, a project manager needs to assign a project management team to ease the process of planning and execution of this project. Last stage, initiating phase, the project manager needs to perform a project review to determine and implies all the initiating activities to be completed. Once the project is reviewed on and the project planning stage is begun (Watt, 2021).

2.0 Planning

In the planning phase, each project team members need to contribute to make sure all the tasks are completed. The meeting should be conducted for discussing further information and how the project will be terminated. The team needs to discuss the potential ideas and share their information in every meeting. Besides, the user requirement should be taken to know what the user or customers want. The team will identify what the hardware, software and which network need to be purchased. The team also needs to identify what are the vision and mission

regarding the requirement of Universiti Sains Malaysia. The project manager will divide the major project deliverables which is it can improve cost and time of project. The team must know their responsibilities and roles to avoid misleading information occurring in this project. The Work Breakdown Structure (WBS) must be created by team members after the project manager has assigned them to complete all the tasks.

3.0 Executing

Indian Financial System (2021) define executing as a process to implement and design the entire of the project. The executing process can make sure the system could be run smoothly without any problems. Features in this financial information system are to facilitate expansion of financial students and staff matters, to help in allocation students' financial risk and set up an entire payment bills and fines of students. In the executing phase, the project team members will do their training session at our company. The training workshop will start with introducing our staff and lead the user to use the services in the financial system that is provided by SMART Tech. LaMarco (2019) determine the execution of project development of Financial Information System (FIS) as the automation of financial operation. Therefore, the features ought to be include in the financial Information System for Universiti Sains Malaysia are reports, preparation and execution of budgets, financial statements, information for budgeting, analysis and reporting, as well as audit trail.

i. Reports

FIS for USM ought to be developed with the provision of management reporting to accurate levels, these reports can assist the management of the business to make high-level decisions for the direction of USM

ii. Budget preparation and execution

The ideal FIS ought to support the preparation and execution of budget in administration level within USM. The preparation of budget is based on the feature that produces financial reports emanating from the system itself. Whereas the real-time data feature in the system will alert the administration regarding the budget execution within the time frame set.

iii. Financial statement

This feature facilitates the preparation of financial statements. To which it is prepared for both internal use and external stakeholders. The financial statement ought to be produced using accurate and reliable data.

iv. Budgeting, analysis, and reporting

The system will be able to provide information for budgeting, analysis, and reporting. These are the 3 important high-level functions determine by the project manager for USM. It can only be carried out if the data generated is accurate and reliable.

v. Audit trail

This feature will be able to provide an audit trail to facilitate the audit process. One of the functions of financial information system is to record transactions. By maintaining records of every single transaction that occurs within USM, the system makes it possible to carry out an audit effectively.

4.0 Maintenance and Controlling

According to Rockwell (2021), corrective maintenance can be separated into planned and unplanned tasks. To which it can be used to improve asset health and performance in circumstances where planned and unplanned maintenance occurs. Meanwhile, in an article of adaptive maintenance, it is defined as the enforcement of changes in the monitoring, use or other operational details of a structure in order to prevent unwanted event from happening (Corrosionpedia, 2018).

There are two types of maintenance in this project, corrective and adaptive maintenance. For the corrective maintenance, our team members will troubleshoot if it is necessary to the system. Our team will make sure the contract for maintenance and warranty valid for 3 years onwards. For the adaptive maintenance, our project team will upgrade software, hardware and network used by clients.

3.3 Gantt Chart

3.3.1 Initiation phase

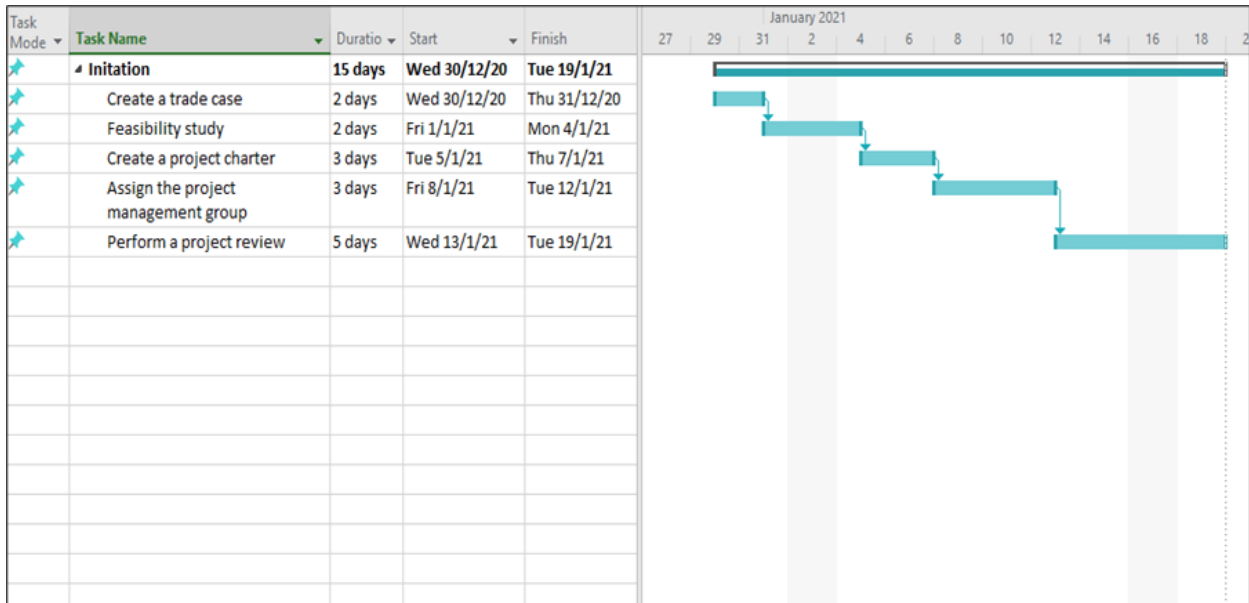


Figure 13 Gantt chart for initiation phase

3.3.2 Planning phase

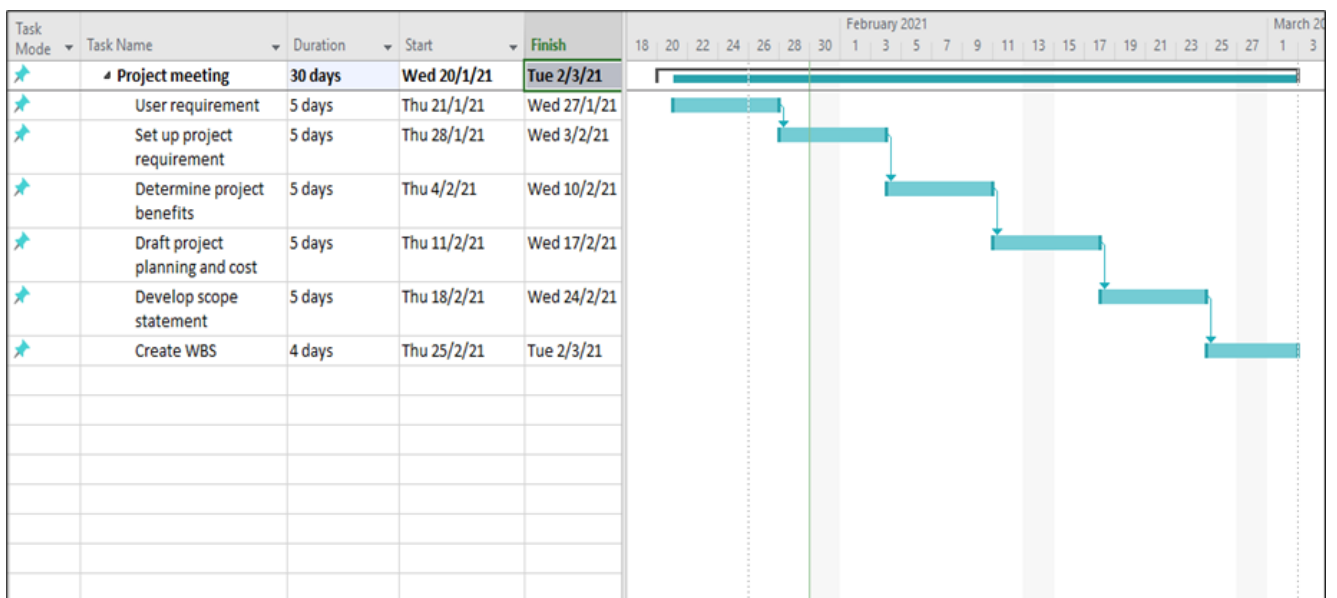


Figure 14 Gantt chart for planning phase

3.3.3 Executing phase

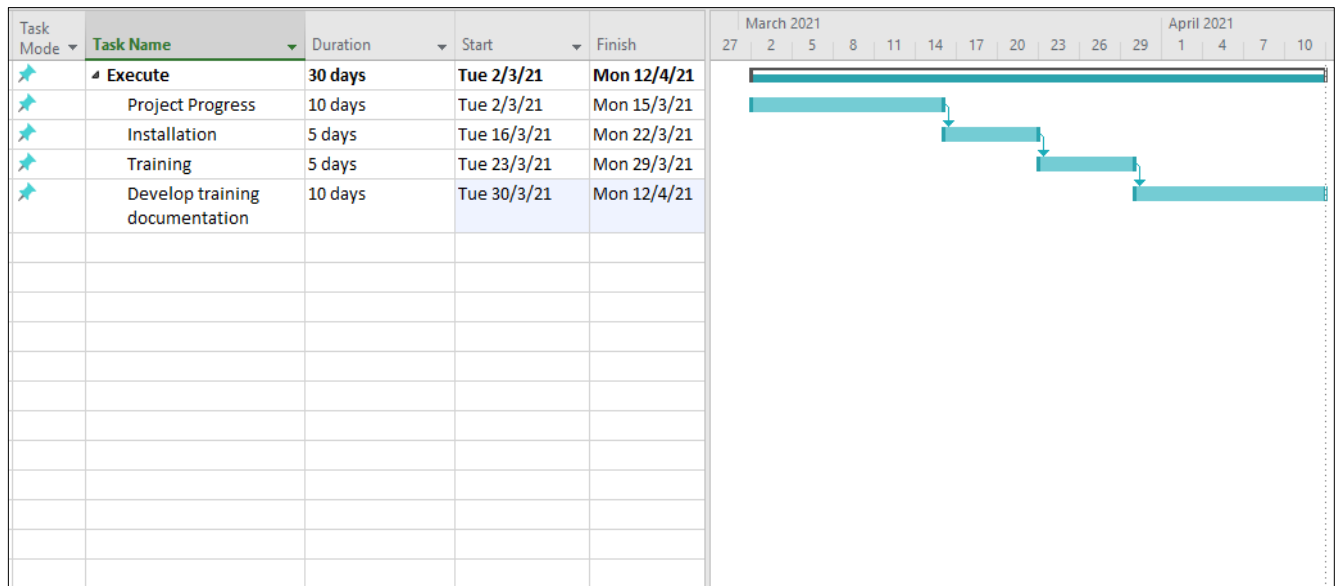


Figure 15 Gantt chart for executing phase

3.3.4 Maintenance and Controlling phase

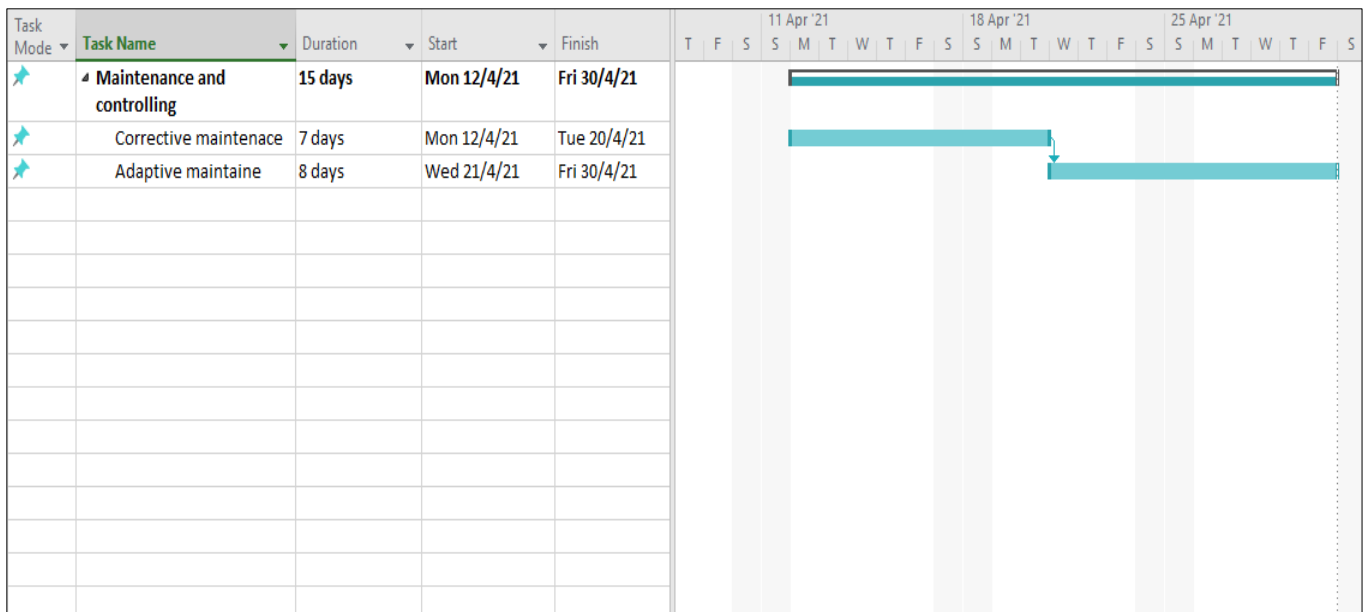


Figure 16 Gantt chart for maintenance and controlling phase

3.4 Network Diagram

Network diagram helps to describe the terminal sequence of the FIS project development for USM. Furthermore, the network diagram can keep track on what task should be done and how it will be done.

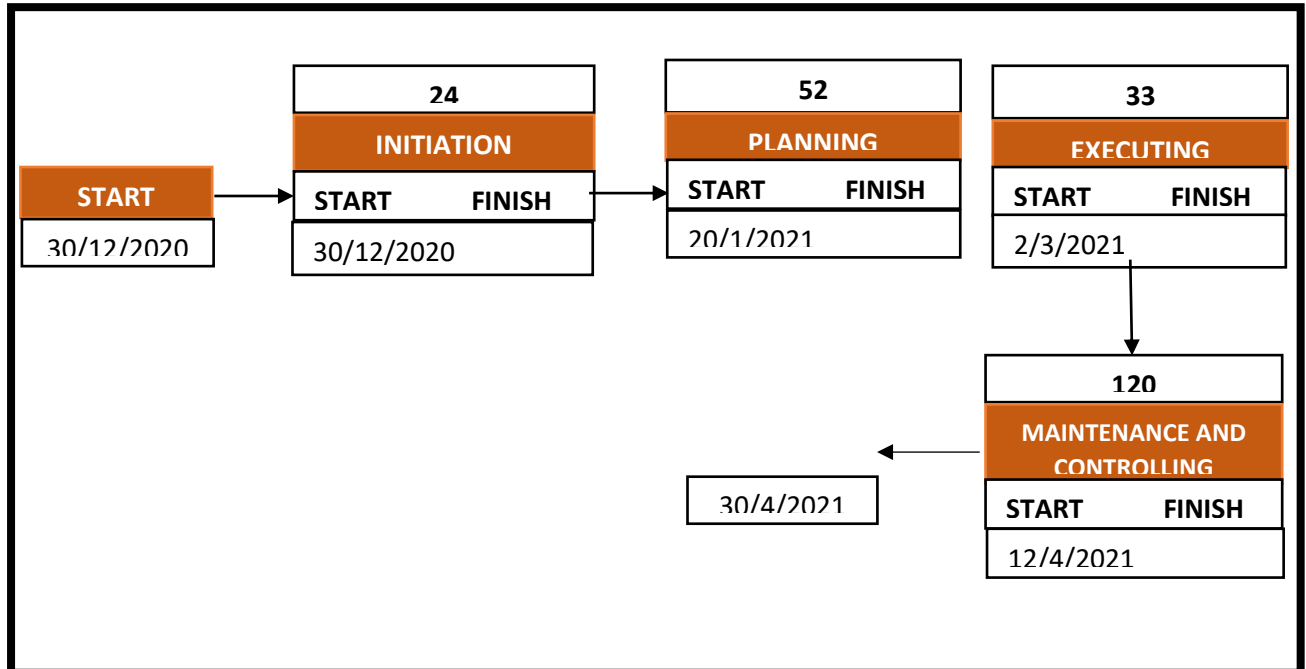


Figure 17 Network diagram

3.5 Appendix (Minutes of meeting)

MINUTES OF MEETING FOR PROJECT DEVELOPMENT

Minutes of the third Committee Meeting of the Committee Members was held on Monday, 1st February 2021 at 10.00 a.m. in the Google Meet.

PRESENT:

- Airul Shazwan Bin Norshahimi (Project Manager)
- Ilani Nur Adriani Binti Jasmin (Deputy Project Manager)
- Mazlina Binti Othman (Programmer)
- Nor Fateha Nadila Binti Mohd Fariq (System Analyst)
- Nurul Fatin Nasuha Binti Mohd Fuzi (Network Expertise)

1. Project Manager Welcome Address

The Project Manager Called the meeting to order at 10.00 am and welcome all the members.

2. Apologies for Absence

No apologies for absence were received at that meeting.

3. Special Business

This meeting will discuss project scope Management.

- Work breakdown structure
 - Create project work breakdown structure
 - Create using Planning, Analysis, Design, Implementation, Maintenance.
- Gantt Chart
 - Build project Gantt chart
- Network Diagram

4. Date, Time and Venue of the Next Meeting

It was also decided that the next meeting will be held on 23 February 2020, in the Google Meet. The time would be confirmed by the secretary later.

5. Close

The project manager thanked all the team members for their participation during the meeting session and adjourned the meeting at 12 p.m.

.....	
Signed by	Date
Mr. Airul Shazwan Bin Norshahimi	
Project Manager	
.....	
Recorded by	Date
Ms. Farisha Amanda Binti Faris	
Secretary	

Figure 18 Minutes of meeting for project development

3.6 References

7. Project Initiation. (2021). Retrieved from <https://opentextbc.ca/projectmanagement/chapter/chapter-7-project-initiation-project-management/>
- Corrosionpedia. (2018). *What is an Adaptive Maintenance? - Definition from Corrosionpedia*. Corrosionpedia. <https://www.corrosionpedia.com/definition/6211/adaptive-maintenance>.
- Indian Financial System-Components and Functions. (2021). Retrieved from <https://data-flair.training/blogs/indian-financial-system/>
- LaMarco, N. (2019). *What Are the Benefits of a Financial Management Information System? Small Business - Chron.com*. <https://smallbusiness.chron.com/benefits-financial-management-information-system-71943.html>.
- Project Planning Phase. (2021). Retrieved from <https://www.method123.com/project-planning-phase.php>
- What is a Work Breakdown Structure? (2021). Retrieved from <https://www.workbreakdownstructure.com/>
- What is corrective maintenance? (2021). Retrieved from <https://www.fiixsoftware.com/corrective-maintenance/>
- What is Project Scope Management?. (2021) Retrieved from <https://www.invensislearning.com/articles/pmp/what-is-project-scope-management>

4.0 – PROJECT COST MANAGEMENT

4.1 Introduction

According to Toliver (2018) cost management is the process of estimating, allocating, and controlling the costs in a project. Project Cost Management is focusing on the process of planning and controlling the budget of project. It involved process of executing the project under the planned budget. While according to the Project Management Institute (2004) in Project Management Body of Knowledge (PMBOK) Guide, Project Cost Management includes the processes required to ensure that the project is completed within the approved budget. The project cost management closely involve with budgeting, estimating, funding and controlling the cost to ensure the project can be completed within the time and budget. By having project cost management, it allows a business to predict coming expenses in order to reduce the chances of it going over budget. The project cost management involve three major process include resource planning, cost estimating, cost budgeting and control. By having project cost management, it helps to avoid over budget after the budgeting process has been done.

4.2 Project Cost Estimates

4.2.1 Project Cost estimates

Table 9 Project cost estimate

Project cost estimate					
	Unit/Hours	Cost/Unit/Hr	Subtotals	WBS Level 2 Totals	% of total
WBS Items					
1. Project Management				RM49,600.00	17%
Project Manager	160	RM90.00	RM14,400.00		
Project team members	640	RM55.00	RM35,200.00		
2. Hardware				RM15,000.00	5%
Handheld devices (PC)	5	RM2,000.00	RM10,000.00		
Servers	5	RM1,000.00	RM5,000.00		
3. Software				RM126,920.00	43%
Licensed software	5	RM4,000.00	RM20,000.00		
Software development			RM106,920.00		
4. Testing (10% of total hardware and software costs)			RM14,192.00	RM14,192.00	5%
5. Training and Support				RM42,700.00	14%
Trainee cost	3	RM1,000.00	RM3,000.00		
Travel cost	3	RM1,500.00	RM4,500.00		
Project team members	640	RM55.00	RM35,200.00		
subtotal			RM248,412.00		
6. Reserves (20% of total estimate)			RM49,682.40	RM49,682.40	17%
Total Project cost estimate				RM298,094.40	100%

4.2.2 Software development estimates

Table 10 Software development estimate

Software Development Estimate			
1 Labor estimate	Units/Hours	Cost/Unit/Hour	Subtotals
Project team estimate	640	RM55.00	RM35,200.00
Total labor estimate			RM35,200.00
2. Function point estimate	Quantity	Conversion Factor	Function Points
External inputs	2	2	4
External interface files	3	3	9
External outputs	3	5	15
External queries	4	6	24
External internal tables	5	4	20
Total function points			72
Java 2 language equivalency value			28
Source lines of code (SLOC) estimate			2016
Productivity $\times$ KSLOC ^{Penalty} (In months)			29.28
Total labor hours (27 hours/function point)			1944
Cost/labor hour (RM55/hour)			RM55.00
Total function point estimate			RM106,920.00

4.2.3 Project cost baseline

Table 11 Project cost baseline

Project Cost Baseline					
WBS Items	Month 1	Month 2	Month 3	Month 4	Totals
1. Project Management					
1.1 Project Manager	RM3,600.00	RM3,600.00	RM3,600.00	RM3,600.00	RM14,400.00
1.2 Project team members	RM8,800.00	RM8,800.00	RM8,800.00	RM8,800.00	RM35,200.00
2. Hardware					
2.1 Handheld devices (PC)		RM5,000.00	RM5,000.00		RM10,000.00
2.2 Servers		RM2,500.00	RM2,500.00		RM5,000.00
3. Software					
3.1 Licensed software		RM10,000.00	RM10,000.00		RM20,000.00
3.2 Software development	RM16,038.00	RM64,152.00	RM26,730.00		RM106,920.00
4. Testing			RM14,192.00		RM14,192.00
5. Training and Support					
5.1 Trainee cost				RM3,000.00	RM3,000.00
5.2 Travel cost				RM4,500.00	RM4,500.00
5.3 Project team members			RM17,600.00	RM17,600.00	RM35,200.00
6. Reserves (20% of total estimate)	RM9,936.48	RM19,872.96	RM14,904.72	RM4,968.24	RM49,682.40
Totals	RM38,374.48	RM113,924.96	RM103,326.72	RM42,468.24	RM298,094.40

4.3 Appendix (Minutes of Meeting)

MINUTES OF MEETING FOR PROJECT DEVELOPMENT

Minutes of fourth Committee Meeting of the Committee Members was held on Monday, 23 February 2021 at 10.00 a.m. in the Google Meet

PRESENT:

- Airul Shazwan Bin Norshahimi (Project Manager)
- Ilani Nur Adriani Binti Jasmin (Deputy Project Manager)
- Mazlina Binti Othman (Programmer)
- Nor Fateha Nadila Binti Mohd Fariq (System Analyst)
- Nurul Fatin Nasuha Binti Mohd Fuzi (Network Expertise)

1. Project Manager Welcome Address

The Project Manager Called the meeting to order at 10.00 am and welcome all the members.

2. Apologies for Absence

No apologies for absence were received at that meeting.

3. Special Business

This meeting will be discussing project cost management.

- Project cost estimation
- Overall costing starts from project management, software, hardware, training and support.

4. Date, Time and Venue of the Next Meeting

It was also decided that the next meeting will be held on 1st March 2021, in the Google Meet. The time would be confirmed by the secretary later.

5. Close

The project manager thanked all the team members for their participation during the meeting session and adjourned the meeting at 12 p.m.

.....

Signed by

Mr. Airul Shazwan Bin Norshahimi

Project Manager

.....

Date

.....	
Recorded by	Date
Ms. Farisha Amanda Binti Faris	
Secretary	

Figure 19 Minutes of meeting for project development

4.4 References

- Project Management Institute. (2004). *A guide to the project management body of knowledge (PMBOK guide)*. Newtown Square, Pa: Project Management Institute.
- Toliver, B. L. (2018). Implementing project management plans to control construction costs on military projects in korea (Order No. 10634869). Available from ProQuest Dissertations & Theses Global. (1964393830). Retrieved from <http://search.proquest.com.ezaccess.library.uitm.edu.my/dissertations-theses/implementing-project-management-plans-control/docview/1964393830/se-2?accountid=42518>

5.0 – PROJECT HUMAN RESOURCE MANAGEMENT

5.1 Introduction

Project human resources management is the phases of identifying the process to organize, manage and lead the project team as well (Lewis, George, 2016). The project team is listed by people with assigned roles as well as responsibilities to complete the project. Even though some specific roles and responsibilities as well are assigned, thorough involvement of all team members within project planning as well as decision making is beneficial though. It includes the participation of team members during planning and their expertise in certain skills strengthen the commitment and process to the project. Hence, the roles can be assigned to the persons or groups as well to perform the proposed project. Project team will be involved into plans as well as the decision making from the beginning of the project. Project human resources management consists of the process in planning for human resource management. Planning for human resource management is crucial in which to identify roles, responsibilities, skills required, reporting as well as staffing management plan.

The project management team as known as the core, leadership team is responsible for project planning, controlling, as well as closing the project team. Our project includes human resources planning, acquire and develop project team, and manage the team. For the proposed project of the system development for information system, the company focus on the resources management as such financial budget planning, stakeholders' involvement, project team building as well as other different sectors that contribute towards the development of this project. All these parts and plans need to be maintained and controlled, along with following the rules of resource management policy. Within this project, our company will take in depth planning and record every detail in which needed for the project to be completed. Generally, human resource management comes with organizational structure that deals with specific responsibility as well as decision of assignments, information system and the planning of manpower are also included within organization planning. The planning of organization as well as the search of human resources need to focus on both manpower to plan the functions as well as the implementation of activities need to be future-oriented. Hence, human resource is the important part needed within the project management to ensure the project will be managed sufficiently.

5.2 Project Organizational Chart

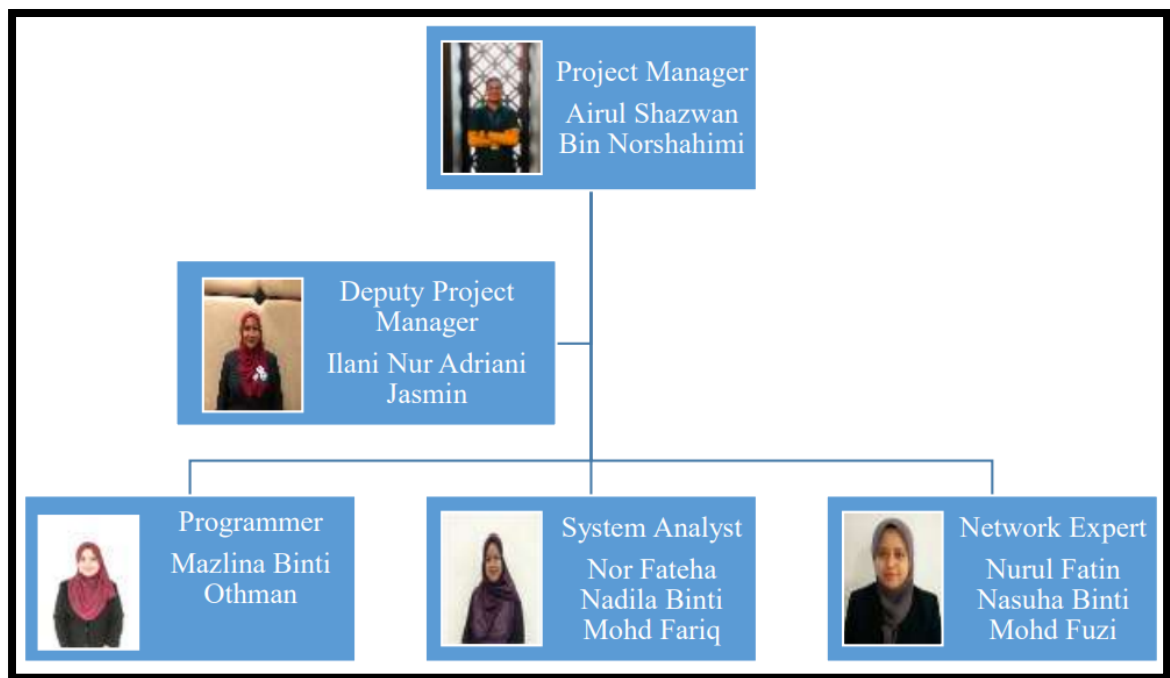


Figure 20 Project organizational chart

5.3 Appendix (Minutes of meeting)

MINUTES OF MEETING FOR PROJECT DEVELOPMENT

Minutes of five Committee Meeting of the Committee Members was held on Monday, 1st March 2021 at 10.00 a.m. in the Google Meet

PRESENT:

- **Airul Shazwan Bin Norshahimi (Project Manager)**
- **Ilani Nur Adriani Binti Jasmin (Deputy Project Manager)**
- **Mazlina Binti Othman (Programmer)**
- **Nor Fateha Nadila Binti Mohd Fariq (System Analyst)**
- **Nurul Fatin Nasuha Binti Mohd Fuzi (Network Expertise)**

1. Project Manager Welcome Address

The Project Manager Called the meeting to order at 10.00 am and welcome all the members.

2. Apologies for Absence

No apologies for absence were received at that meeting.

3. **Special Business**

This meeting will discuss project Human Resource Management.

- Organizational Chart

4. **Date, Time and Venue of the Next Meeting**

It was also decided that the next meeting will be held on 22 March 2021, in the Google Meet. The time would be confirmed by the secretary later.

5. **Close**

The project manager thanked all the team members for their participation during the meeting session and adjourned the meeting at 12 p.m.

.....

Signed by

Mr. Airul Shazwan Bin Norshahimi

Project Manager

.....

Date

.....

Recorded by

Ms. Farisha Amanda Binti Faris

Secretary

.....

Date

Figure 21 Minutes of meeting for project development

5.4 References

Lewis, George. (2016, June 28). Project Human Resource Management. Retrieved from <https://www.projectmanagement.com/blog-post/21150/Project-Human-Resource-Management>

6.0 – PROJECT COMMUNICATION MANAGEMENT

6.1 Introduction

According to PMBOK 6th Edition (2004), project communication management can be defined as significant processes executed in order to ensure that the information needs of the project and its stakeholders are met through the development of artifacts and implementation of activities designed to achieve effective information exchanges. According to a survey report by Project Management Institute (PMI) in 2013, it was identified that due to ineffective communication, one out of five projects is unsuccessful. In order to hinder that from happening, project managers must curate an effective project communication management. Project communication management incorporates various processes to which it determines that relevant project information is delivered to the right team within the right time frame. Effective communication helps in establishing a healthy relationship between diverse stakeholders with varying cultural and organizational backgrounds, expertise level, interests, and perspectives. The combination of the factors could influence the project execution and the final product. The complete process of project communication management is an aggregation of several distinct parts which includes planning communication management to which it involves the development of several approaches to identify stakeholders' information and communication needs. Next, managing communication which incorporates creating, disseminating, keeping, retrieving, and disposal of project communication based on the communication management plan. Lastly, controlling communication to which it includes monitoring and controlling project communication to determine the fulfilment of stakeholders' communication needs.

6.2 Communication Management Plan

According to Schwalbe (2015), a Communications Management Plan (CMP) is defined as a document that guides project communications. This is due to the fact that communication is an essential factor on projects. The plan should even be considered as a part of the overall plan of project management. This is because the designated plan incorporates the needs of the project however it is important to ensure that a written plan is prepared. The main focus of CMP is to advertise project excellent performance by meeting the information needs of the project stakeholders and indicates the goals of the communication efforts to achieve. The intended audience of Smart Tech CMP is the project manager, project team members, project sponsors, senior leaders and other stakeholders whose support is considered significant upon the completion of the project.

Table 12 Communication management plan

STAKEHOLDER	COMMUNICATON APPROACH	FREQUENCY	RESPONSIBILITY	NOTES
Key Stakeholder	Project kick-off meeting with team members	Initial phase of the project, one time only.	Project Management Office	It is highly suggested that both; team and client kick-off meeting take place.
Client Executives	Executive Steering Committee	Monthly- every first Monday of each month	Financial Manager	Review status, milestones on checked, obtained value indicators, key issues.
Client Sponsor	Status Meetings Progress Reports (Email)	Weekly, every Friday at 12 noon	Project Manager	Review development progress, schedule alteration requested, issues.
Development Team	Progress Meetings	Weekly, every Friday at 4pm	Project Manager	Provides input based on the meeting with client sponsor.

6.2.1 Stakeholder Management Strategy

Table 13 Stakeholder management strategy

Name	Position	Internal/ External	Level of Interest	Level of Influence	Potential Management Strategies
Prof Dr. Faisal Rafiq	Vice-Chancellor of USM	External	High	High	Prof Dr. Faisal Fariq is the client of the project. It is essential to keep him update on the progress and remind him that he is a part of the team.
Rayyan Adam B Rayyan Alif	CEO of Smart Tech	Internal	High	High	Mr. Andrew is the CEO of the company who is very professional. Keep him informed of the key constraints and never let anything surpass him.
Airul Shazwan B Norshahimi	Project Manager	Internal	High	High	As the project manager, Airul Shazwan is known to be team-driven, creative minded and well-organized that makes him easy to work with.
Ilani Nur Adriani Bt Jasmin	Deputy Project Manager	Internal	High	Medium	Ilani is the deputy who determine to ensure contingency plan is prepared and ought to be executed with excellence.

Mazlina Bt Othman	Project Programmer	Internal	High	Low	As the project programmer, Mazlina is multitasking, as she is able to work on the framework and ensure the progress is done smoothly.
Nor Fateha Nadial Bt Mohd Fariq	System Analyst	Internal	High	Low	As system analyst, Fateha is known to be very meticulous with her work. She ought to finish her tasks in orderly manner.
Nurul Fatin Nasuha Bt Mohd Fuzi	Network Expert	Internal	High	Low	As the team's network expert, Fatin is an important person to which she is responsible of connection from all aspects.
Khoo Boon Lim	CEO of Rapid Cloud	External	High	Medium	The CEO of Rapid Cloud is the sponsor of several well-established projects. Therefore, it is importance to provide him with the status on the project development.
Joshua A/L Muthu	Software Engineer Officer at Rapid Cloud	External	Medium	Low	Joshua works with Rapid Cloud. Therefore, his contribution is significant to the project which is why it is vital to ensure all progress is within the time frame.

6.2.2 Stakeholder Communication Analysis

Table 14 Stakeholder communication analysis

STAKHOLDER	DOCUMENT NAME	DOCUMENT FORMAT	CONTACT PROFILE	DUE
VC of USM	Monthly status report	Hard copy and meeting	Prof Dr. Faisal Rafiq	First week of the month
CEO of Smart Tech	Monthly status report	Hard copy and meeting	Rayyan Adam B Rayyan Alif	First week of the month
Project Management Office	Weekly status report	Hard copy and meetings	Airul Shazwan B Norshahimi	First week of the month
Internal Management	Weekly status report	Email	Ilani Nur Adriani Mazlina Othman Nor Fateha Nadila Nur Fatin Nasuha	First week of the month
CEO of Rapid Cloud; officer	Weekly status report	Email	Khoo Boon Lim Joshua A/L Muthu	First week of the month

6.2.3 Media Choice Table

Based on an article from Technopedia (2017), communication media can be defined as a medium of delivering and receiving data or information. In the context of telecommunication, it is considered as medium of transmission and storage tools or channels for data storage and transmission.

Table 15 Media choice

How well medium is suited to:	Meeting	phone call	E-mail	Notice
Assessing commitment	1	2	1	1
Building consensus	1	2	3	3
Mediating a conflict	1	2	3	3
Resolving a misunderstanding	1	3	2	3
Addressing negative behavior	1	1	1	1
Expressing support or appreciation	1	1	2	2
Encouraging creative thinking	1	2	3	1
Making an ironic statement	1	3	2	2
Conveying a reference document	3	3	3	3
Reinforcing one's authority	3	3	3	1
Providing a permanent record	1	3	2	1
Maintaining confidentiality	1	1	3	2
Conveying simple information	2	1	2	3
Asking an informational question	3	1	1	3
Making a simple request	2	1	1	2
Giving complex instruction	1	3	1	3
Addressing many people	1	3	1	1

KEY INDICATOR: 1 = Excellent, 2 = Adequate, 3 = Inappropriate

6.2.4 Monthly/Weekly Progress Report

Table 16 Monthly / weekly progress report

Project Name: Implementation of Financial Information System at Universiti Sains Malaysia
Project Manager: Airul Shazwan Bin Norshahimi
Work completed this reporting period: -
Work to be completed upon the next reporting period: Project Charter Team Contract
What went smoothly and why: The implementation of the FIS for Universiti Sains Malaysia was initiated with excellence. The team members are aware with their roles and responsibilities and work meticulously with tasks given.
Constraint faced and why: The FIS framework is need modification to certain extent. The is a need to clarify this constraint within the team and provide effective solution soon.
Suggestions/issues: Arrange a meeting with team member to provide solution and another meeting with stakeholder to propose the solution and proceed from there.
Project changes: The developer ought to keep providing innovative changes that would make the FIS user-friendly and would be sustainable for a long period of time.

6.2.5 Milestone report

MILESTONE	STATUS	RESPONSIBLE OFFICER	ISSUES / COMMENTS
INITIATING PHASE			
Identifying stakeholders	Completed	Airul Shazwan	Excellent remarks
Signing Project Charter	Completed	Airul Shazwan	Excellent remarks
Organizing project kick-off meeting	Completed	All team members	Excellent remarks
PLANING PHASE			
Signing team contract	Completed	Nur Fatin Nasuha	Excellent remarks
Completing scope statement	Completed	Nur Fatin Nasuha	Excellent remarks
WBS Completed	Completed	Airul Shazwan	Several constraints highlighted
Completion of list of prioritized risks	Completed	Ilani Nur Adriani	Reviewed with stakeholders
Completion of schedule and cost baseline	Completed	Airul Shazwan	Excellent remarks
EXECUTING PHASE			
Completion of survey	Completed	Nor Fateha Nadila	Excellent remarks
Completion of experts' reference	Completed	Nor Fateha Nadila	Excellent remarks
Completion of user requested features	Completed	Mazlina Othman	Several constraints highlighted
MONITORING AND CONTROLLING PHASE			
Progress report	Completed	All team members	Excellent remarks

CLOSING PHASE			
Completion of final project presentation	Incomplete	All team members	Several constraints highlighted
Sponsor signing-off on project	Completed	Airul Shazwan	Excellent remarks
Completion of final project report	Completed	Ilani Nur Adriani	Excellent remarks

6.3 Appendix (Minutes of meeting)

MINUTES OF MEETING FOR PROJECT DEVELOPMENT

Minutes of six Committee Meeting of the Committee Members was held on Monday, 23 March 2021 at 10.00 a.m. in the Google Meet

PRESENT:

- Airul Shazwan Bin Norshahimi (Project Manager)
- Ilani Nur Adriani Binti Jasmin (Deputy Project Manager)
- Mazlina Binti Othman (Programmer)
- Nor Fateha Nadila Binti Mohd Fariq (System Analyst)
- Nurul Fatin Nasuha Binti Mohd Fuzi (Network Expertise)

1. Project Manager Welcome Address

The Project Manager Called the meeting to order at 10.00 am and welcome all the members.

2. Apologies for Absence

No apologies for absence were received at that meeting.

3. Special Business

This meeting will be discussing project communication management.

- Project communication management
- Communication management plan
- Stakeholder management strategy
- Media choice
- Milestone report

4. Date, Time and Venue of the Next Meeting

It was also decided that the next meeting will be held on 19 April 2021, in the Google Meet. The time would be confirmed by the secretary later.

5. Close

The project manager thanked all the team members for their participation during the meeting session and adjourned the meeting at 12 p.m.

.....

Signed by

Mr. Airul Shazwan Bin Norshahimi

Project Manager

.....

Date

.....

Recorded by

Ms. Farisha Amanda Binti Faris

Secretary

.....

Date

Figure 22 Minutes of meeting for project development

6.4 References

Chand, S. (2019). *Project Communication Management: How To Ensure Success? Edureka*. Edureka. <https://www.edureka.co/blog/project-communication-management/>.

Project Management Institute, Inc. The Essential Role of Communications. (2013). *The High Cost Of Low Performance: The Essential Role Of Communications organizational*.

Techopedia. (2017). *What is Communication Media? - Definition from Techopedia*. Techopedia.com. <https://www.techopedia.com/definition/14462/communication-media>.

7.0 – Project Risk Management

7.1 Introduction

Within project management, the assessment towards risk is important to take part in order to prevent any possible risk that might occur throughout the process of developing system. Project risk management can be defined as a process to assess, evaluate, as well as mitigate or prevent any potential those risks into a project that might potentially impact the predictable outcomes (Watt, 2021). Hence, project manager is in charge of keeping an eye on the risk management process all over the given project duration. To manage the risk effectively, project manager need to have a clear understanding of their objectives in identifying any possible barriers in which it will impact the ability of team in order to produce results.

Generally, the objectives of project risk management that exist depends on the likelihood of impact from the positive events, might as well decrease the likelihood of impact from the negative events within this project (Rajman Md Rawi, n.d.). Hence, by addressing possible risk and the action that might happened during work progress in which it will create a guideline that can be referred in future. Thus, by assessing possible risk, this activity will help our project team in order to overcome the problems efficiently in order to ensure the progress is on the right track.

7.2 List of Prioritized Risks

Table 17 List of prioritized risks

RANK	POTENTIAL RISK
1	System security
2	System breakdown
3	Changes within project workflow
4	Over budgeting
5	Human resource expertise
6	Estimating or scheduling errors
7	Unplanned work that must be accommodated
8	Clients fail to obey with system usage
9	Vendors forfeit from the project

7.3 Risk Register

The risk register table below illustrates various kind of possible risks that might be occurred by looking at every phase of development. The potential risks fall under its own categorization in which occurred by different causes along with its root problem and responses as well. This method also illustrates how the impact towards the project development thoroughly with other aspect and its possibility to happen.

Table 18 Risk register

Risk	Category	Cause	Triggers	Potential Response	Owner	Probability	Impact	Status
System security	Technical risk	Exposed to hackers	Security patches and old security tools	Updated software	Programmer	Low	High	Updated software supplied with sufficient security patches
System breakdown	Technical risk	Coding problem	Old coding approach did not match with technology	Migrate to updated coding language	Programmer	Low	High	Coding must aligned with latest hardware and software
Changes within project workflow	Technical risk	System does not meet with user requirements	Workflow might change over the time	Apply system improvement	System Analyst	Low	Medium	Always check and review the system and their user needs
Over budgeting	Financial issue	Exceed used of budget	Unclear to identify project requirements	Any purchases need to follow within budget allocated	Project Manager	Low	High	Sufficient used of budget in purchasing equipment

Human resources expertise	Governance risk	Progress delayed in certain phases	Project is not able to finish within project timespan	Hire external expertise	Project Manager	Low	High	Receive help from external stakeholders for phases in project management
Estimating/scheduling errors	Technical risk	Progress did not meet at desirable timeline	Delaying in performing task followed with schedules	Track every progress at completion and make necessary adjustments.	Project Manager	Low	High	Build 10% contingency on cost and scheduling as well as track daily schedules and agenda item within project team meeting.
Unplanned works that need to be accommodated	Human resource risk	Unplanned works that might occur in the middle of progress	Numbers of unexpected issue circumstances in short time to be completed	Provide project manager with plan of action, includes impact on time, cost and quality of project development.	Project Team Manager	Low	High	Team managers attending scheduling workshops.
Client fails to obey with system usage	Technical risk	Clients are not participating within training session	System is not fully used by the user	Deliver video recording as a method of training	System Analyst	Medium	High	Clients able to re-watch the video to learn how to use the system
Vendors forfeit from the project	Market risk	Vendor loss interest in project development	Vendor does not accept with price quotation	Provide agreement in black and white with the vendor.	Project Manager	Low	High	Develop good relationship with vendors

7.4 Appendix (Minutes of meeting)

MINUTES OF MEETING FOR PROJECT DEVELOPMENT

Minutes of seven Committee Meeting of the Committee Members was held on Monday, 19 April 2021 at 10.00 a.m. in the Google Meet

PRESENT:

- Airul Shazwan Bin Norshahimi (Project Manager)
- Ilani Nur Adriani Binti Jasmin (Deputy Project Manager)
- Mazlina Binti Othman (Programmer)
- Nor Fateha Nadila Binti Mohd Fariq (System Analyst)
- Nurul Fatin Nasuha Binti Mohd Fuzi (Network Expertise)

1. Project Manager Welcome Address

The Project Manager Called the meeting to order at 10.00 am and welcomed all the members.

2. Apologies for Absence

No apologies for absence were received at that meeting.

3. Special Business

This meeting will be discussing project risk.

- List of prioritized risk
- Risk Register

4. Date, Time and Venue of the Next Meeting

It was also decided that the next meeting will be held on 30 April 2021, in the Google Meet. The time would be confirmed by the secretary later.

5. Close

The project manager thanked all the team members for their participation during the meeting session and adjourned the meeting at 12 p.m.

.....

Signed by

Mr. Airul Shazwan Bin Norshahimi

Project Manager

.....

Date

.....	
Recorded by	Date
Ms. Farisha Amanda Binti Faris	
Secretary	

Figure 23 Minutes of meeting for project development

7.5 References

- Rajman Md Rawi. (2016, May 19). Project Risk Identification for New Project Manager. Retrieved from <https://www.projecttimes.com/articles/project-risk-identification-for-new-project-manager.html>
- Watt, A. (2014). 16. Risk Management Planning. Retrieved from <https://opentextbc.ca/projectmanagement/chapter/chapter-16-risk-management-planning-project-management>

8.0 – CLOSING THE PROJECT

8.1 Introduction

Close project or closing phase management is the process at the last stage in which arrangements are concluded and settled and all the things or goods negotiated are resolved (Lucidchart blog, 2019). Our project team will evaluate when all testing has been fully done in compliance with the requirements and all end product customers are pleased. In addition, as a final analysis for potential references, reports need to be revised to reflect the final findings. The date starts this project in December until April. We take four months to complete this tender. Thus, the team will be able to know what to implement in the project development, the time required is very essential, it is considered limited because we need to carefully consider what will be included in the task contained in the project. We specifically are able to know the things that the user wants to include in the system. The project manager creates a client acceptance form that can be used to record the client's sign-off and officially bring the project to a close. So, we will provide a client acceptance form that contains information about the end product that client will accept. Using this form will officially bring your project to a close and give us an opportunity to discuss key aspects of the project. In the end it will give us a mutually agreed upon outcome.

8.2 Client Acceptance / Project Completion Form

Client Acceptance Form	
Implementation of Financial Information System for Universiti Sains Malaysia (USM) Created by Smart Tech	
Project: Implementation of Financial Information System for Universiti Sains Malaysia (USM) (Dashboard)	
This document has been issued by: [Person Issuing Document]	Date Issued:
The Project Outcome has been measured against its acceptance criteria and has been formally accepted on behalf of the customer. The project may now be closed.	
Additional Comments about the Customers' Acceptance:	
Recorded Shortfalls of the Final Project Outcome (if any):	
Executive / Sponsor:	Signature: _____ Name: _____ Date: _____
Project Manager:	Signature: _____ Name: _____ Date: _____

Figure 24 Client acceptance / project completion form

8.3 Lessons Learned Report

The project manager knows the importance of capturing lesson. Learning is essential as it is good for the organization and future project. The lessons learned are the documents documentation that contain information which reflect both the positive and negative experience of the project. However, lessons learned may be identified and documented at any point during the project's life cycle. Here we include examples of lesson reports learned that will be produce at the end of the project management activity (Semczuk, 2021).

8.4 Appendix

Project Name:	Implementation of Financial Information System for Universiti Sains Malaysia (USM)
Prepared by:	Airul Shazwan Bin Norshahimi
Date	27 December 2020

Project Close Out Discussion	
A lesson learned was held on 30/04/2021	
Attendees	Absent
Airul Shazwan Bin Norshahimi	
Nur Adriani Binti Jasmin	
Mazlina Binti Othman	
Nor Fateha Nadila Binti Mohd Fariq	
Nurul Fatin Nasuha Binti Mohd Fuzi	
List Project's biggest success	
Description	Factors that contribute
Follow the time giving	Team member follow all the Gantt-chart that being setup before all work getting started

Follow the budget stated	All the expenses being monitor and spent based on given.
List area of potential improvement	
Category	Lesson Learned
Project Management	Project management need to determine if its project should continue with a project structure in place.

8.5 References

Semczuk (n.d.). Lessons-learned-template-project-lessons-learned-report-d1 lessons learned template: Lessons learned, Business plan template, Report template. Retrieved from <https://www.pinterest.com/pin/215469163406648555/>

Lucidchart blog. (2019). *Get It Done: Nailing the Project Management Closure Process*. 7 Steps to Nail the Project Management Closure Process | Lucidchart Blog. <https://www.lucidchart.com/blog/nailing-the-project-management-closure-process>.
